






Works complete (22 & 23 July)

Tues 22 July & Wed 23 July

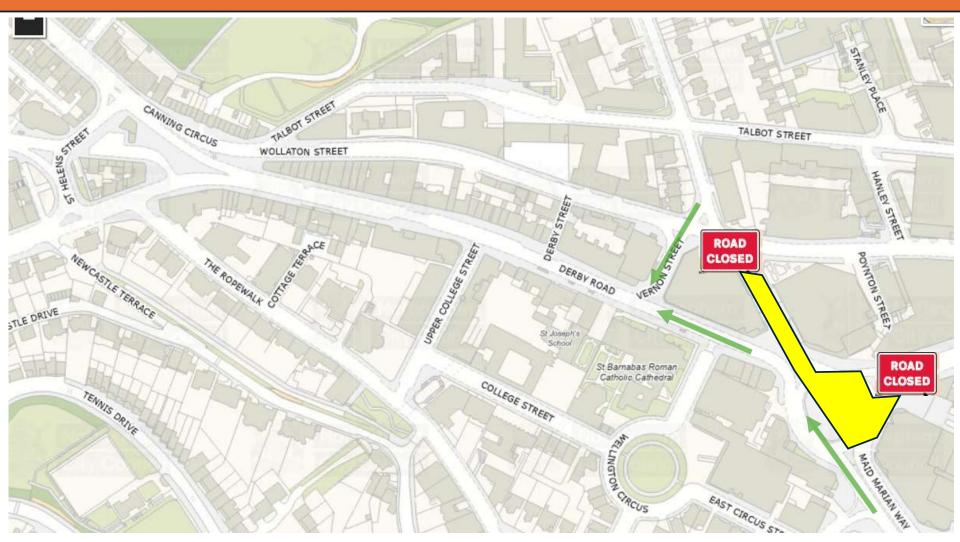




Original: Mon 28 July

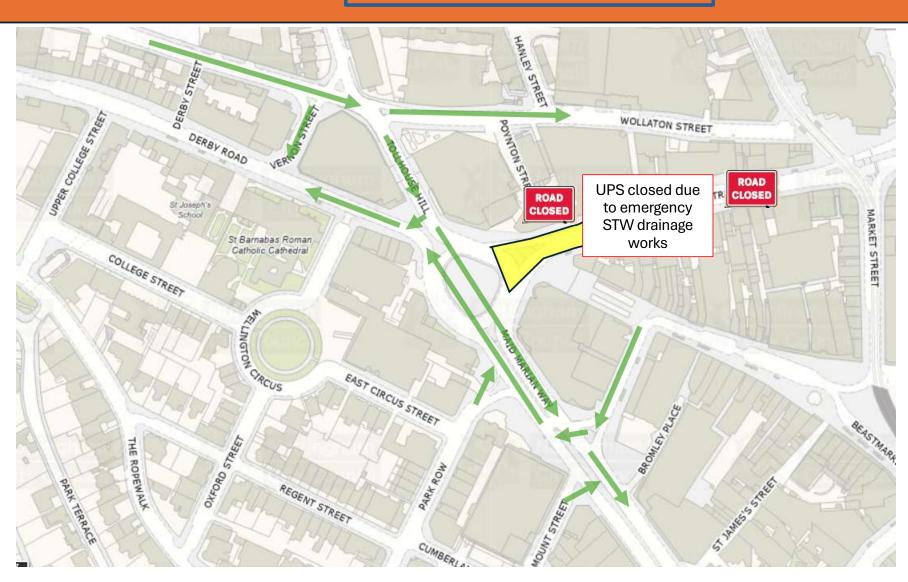




Original: Tues 29 July

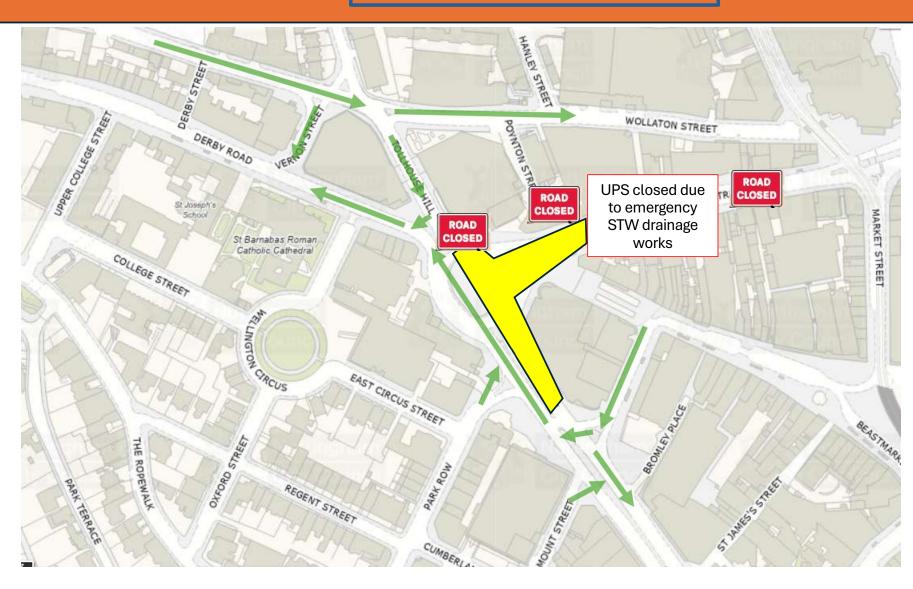




riginal: Weds 30 July

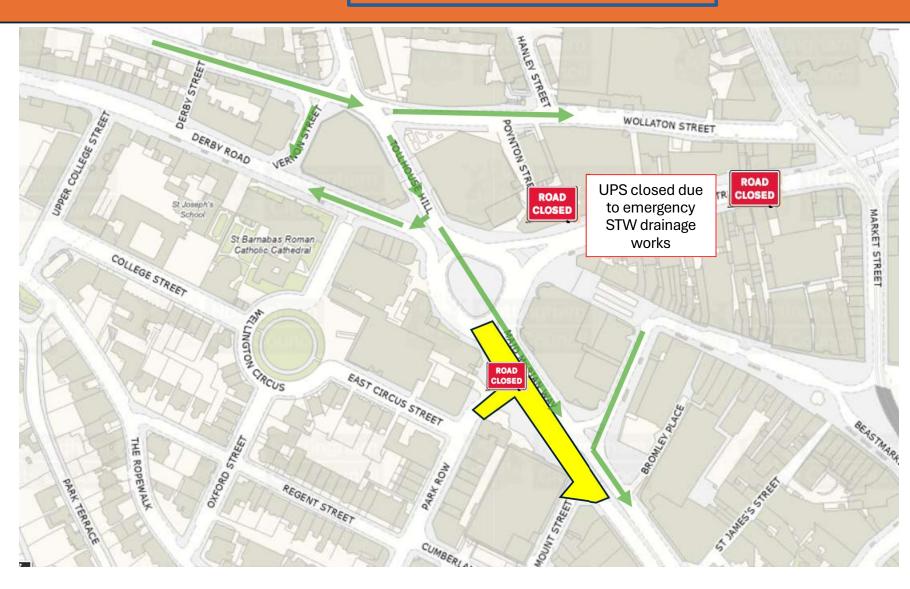



Original: Thurs 31 July

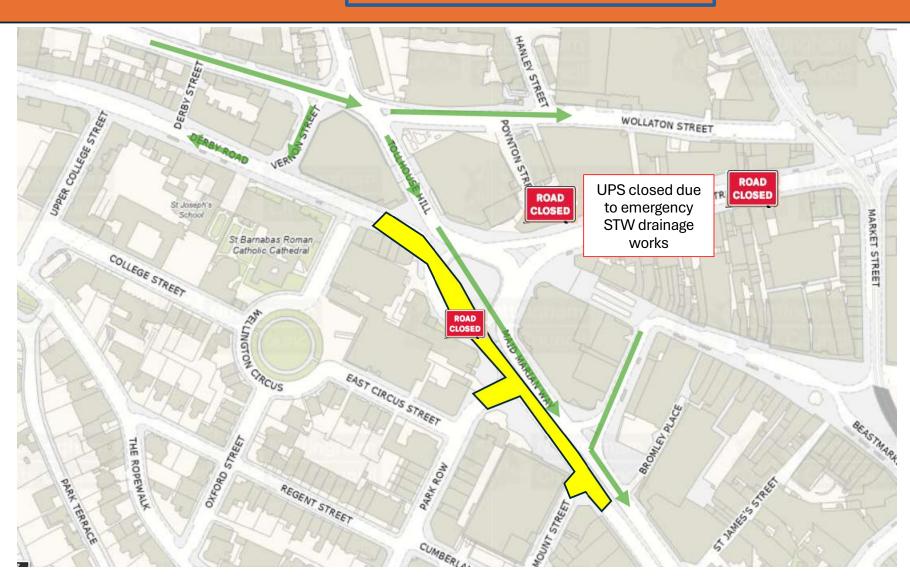




Works complete (31 July)

Thurs 31 July to Sat 2 Aug

Original: Thurs 31 July to Sat 2 Aug

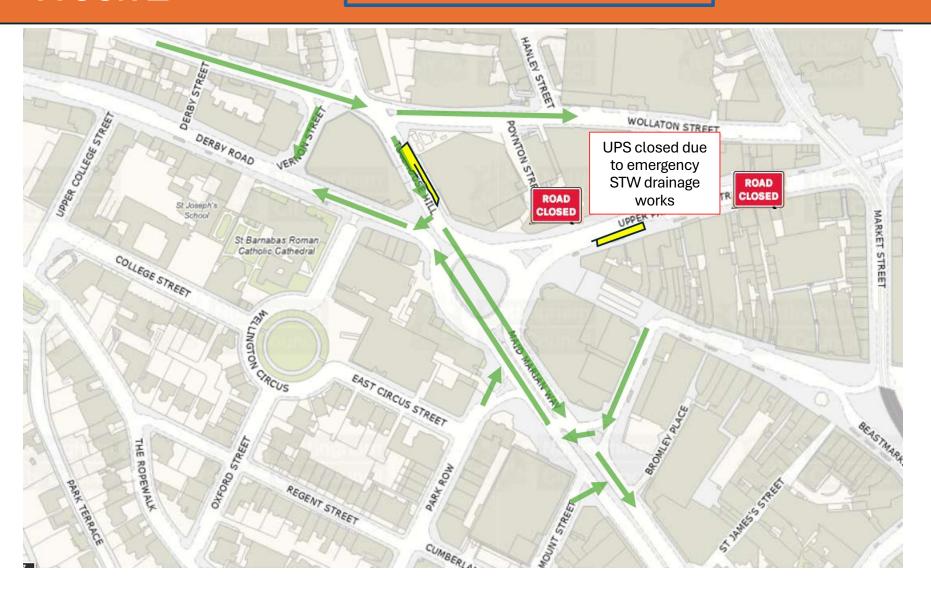





Hardipave application to bus stops on THH and UPS

Bus stop out of use 8pm Thursday 31st July to 8am Saturday 2nd August


Original: Mon 4 Aug




Works complete (5 & 6 Aug)

Tues 5 Aug & Weds 6 Aug

Original: Tues 5 Aug & Weds 6 Aug

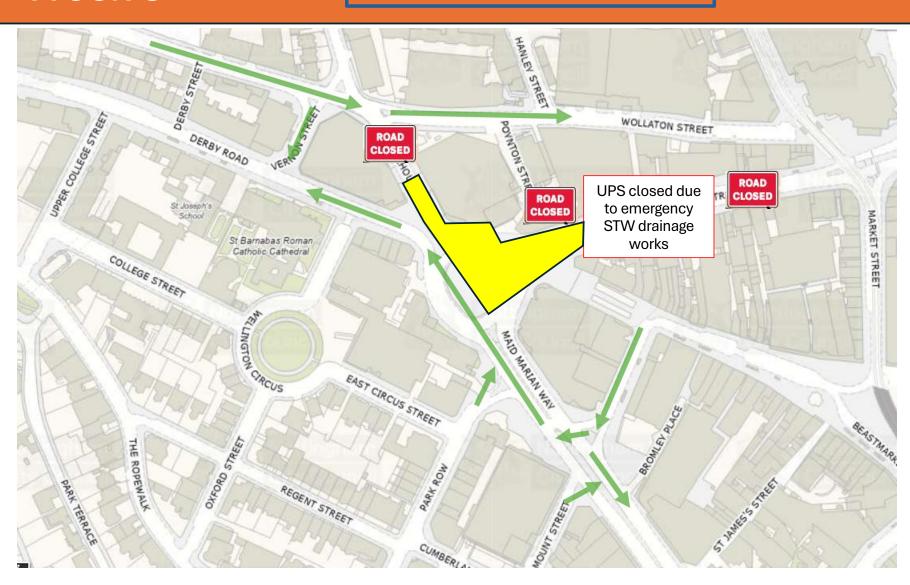






Placement of surface course

Closures in place 22.00 to 06.00

Original: Tues 12 Aug

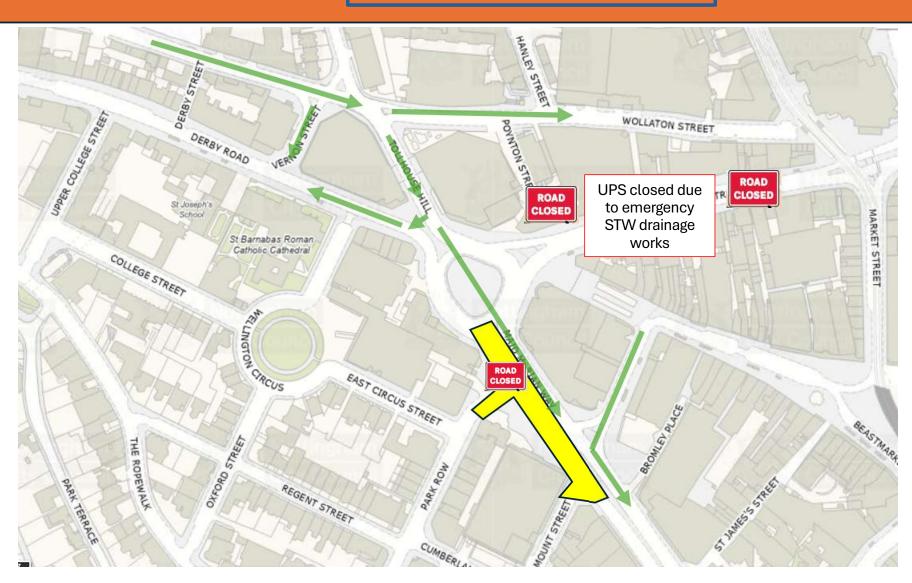



Placement of surface course

Works area

Closures in place 22.00 to 06.00

Mon 11 & Tues 12 Aug

Original: Weds 13 Aug & Thurs 14 Aug






Placement of surface course

Closures in place 22.00 to 06.00

Weds 13 Aug

Original: Mon 18 Aug






Placement of surface course

Tues 26 Aug

Original: Thurs 24 July

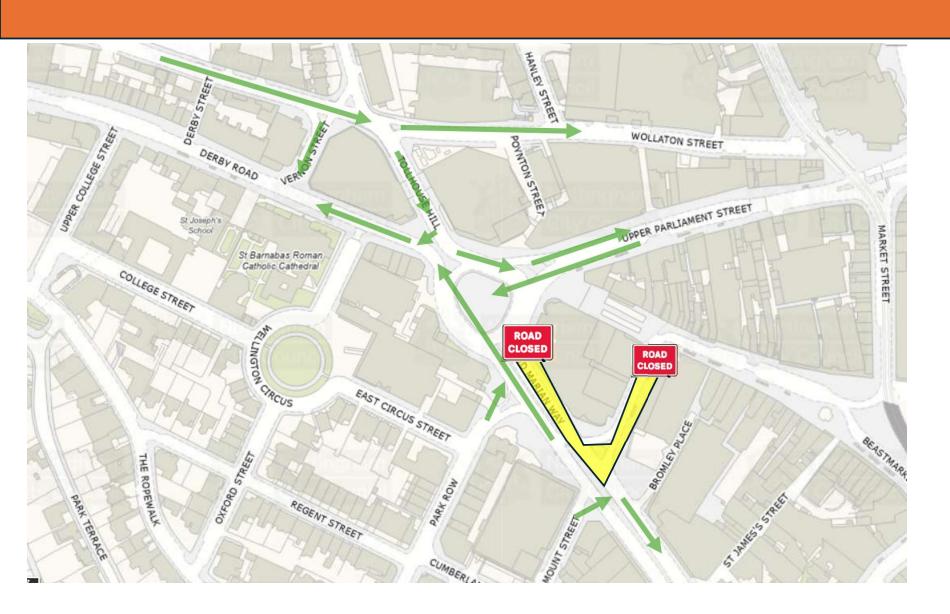






Works area

Works up to top of binder course

These works will only take place once the emergency Severn Trent Water drainage works are complete on UPS.

Weds 27 & Thurs 28 Aug

Original: Thurs 7 and Mon 11 Aug

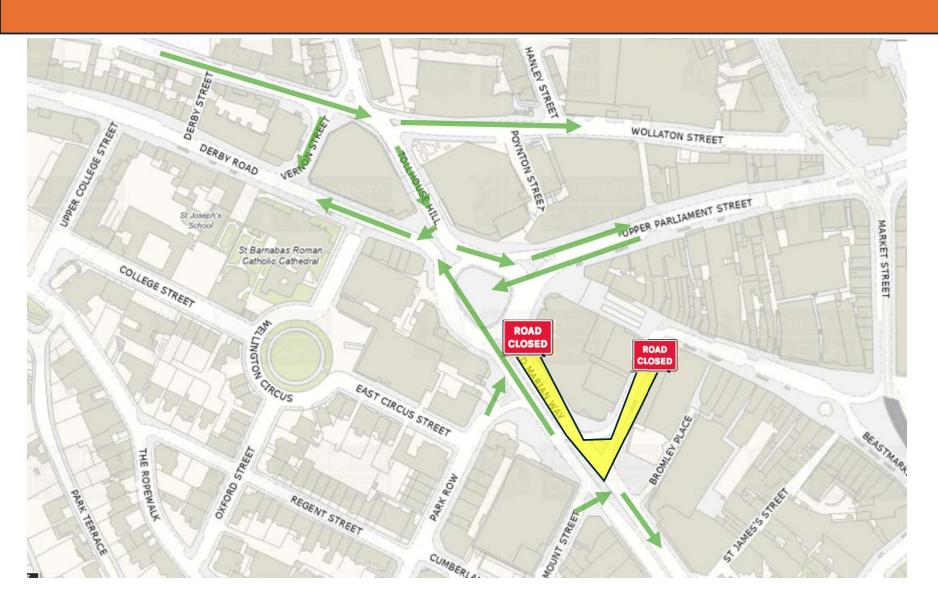



Placement of surface course

These works will only take place once the emergency Severn Trent Water drainage works are complete on UPS.
